



T-NOC NOKIA AMS Application Functional Acceptance Test Procedure Document

Tender Ref. No.: TSTS/CS/RFP-T-FIBER-MSI/2018)

Telangana Fiber Grid Corporation Ltd.

(T-FIBER)

Government of Telangana

JANUARY 30, 2026



Revision History

Revision No.	Date of Submission	Description of Revision	Prepared By	Date of submission for Review	Review completed Date
1.0	25 th Jun22	Initial Version	L&T/Nokia	25-02-2022	25-02-2022
1.1	13 th Jul22	ATP Updated as per T-Fiber recommendation	L&T/Nokia	13-07-2022	22-08-2022
1.2	17 th Feb25	Test cases updated in ATP document	L&T	17-02-2025	09-03-2025
1.3	08 th Apr25	Added more Test cases in ATP document	L&T	08-04-2025	15-04-2025
1.4	19 th Apr25	Incorporated Test cases as per observations in review	L&T	19-04-2025	29-04-2025
1.5	27 th Nov25	Incorporated Test cases as per observations in review	L&T	27-11-2025	16-01-2026
1.6	20 th Jan26	Incorporated Test cases as per observations in review	L&T	20-01-2026	29-01-2026
1.7	30 th Jan26	Incorporated APIs in a required format as per observations in review	L&T	30-01-2026	
Prepared by		Reviewed By		Approved by	
Sayyad Pasha (SME GPON – L&T)		Ranganadham Srinivasa Rao (Network Head – L&T)		Sidda Reddy (Project Director – L&T)	



Contents

1 Introduction	5
2 Test Cases	6
Test Case 1: Validation of IP address for AMS application primary, secondary and DR	7
Test Case 2: AMS Server Storage Sizing and Utilisation	7
Test Case 3: Verify Application Version details.....	8
Test Case 4: AMS application License Verification.....	8
Test Case 5: OLT Addition in AMS.....	9
Test Case 6: OLT Deletion in AMS.....	9
Test Case 7: ONT Addition	10
Test Case 8: ONT Deletion.....	10
Test Case 9: OLT Location Name Modification in AMS	11
Test Case 10: Node Reachability Test.....	11
Test Case 11: ONT Status Test in AMS (Dying Gasp Alarm)	12
Test Case 12: ONT Serial Number Modification from AMS	12
Test Case 13: Service Configuration from AMS With Vlan Translation in Bridge Mode.....	13
Test Case 14: Service Configuration from AMS Without Vlan Translation in Bridge Mode	13
Test Case 15: Service Configuration from AMS with Vlan Translation for Route Mode	14
Test Case 16: Service Configuration from AMS Without Vlan Translation for Route Mode	14
Test Case 17: Service Configuration from AMS in Bridge Mode Tagged.....	15
Test Case 18: Service Configuration from AMS for Q&Q services	15
Test Case 19: Configuration from AMS for IPv6 Service	16
Test Case 20: Service Deletion from AMS	16
Test Case 21: Service Upgradation/Degradation	17
Test Case 22: User Management with L1, L2, L3 Privileges	17
Test Case 23: AMS Password Policies	18
Test Case 24: Alarm synchronisation with OSS	18
Test Case 25: OLT/ONT Inventory synchronisation with OSS.....	19
Test Case 26: AMS functionality with syslog server.....	19
Test Case 27: AMS functionality with NTP server	20
Test Case 28: OLT/ONT inventory report generation from AMS.....	20
Test Case 29: Alarms report generation from AMS	21



Test Case 30: Service inventory report generation from AMS	21
Test Case 31: Bandwidth Profiles report generation from AMS	22
Test Case 32: AMS DB Backup Operation.....	22
Test Case 33: AMS DB Backup Restoration	23
Test Case 34: Node Backup Procedure	23
Test Case 35: ONT Upgrade from AMS	24
Test Case 36: Application Primary and Secondary Switch over by server shutdown	24
Test Case 37: Application Primary and Secondary Switch over by server reboot	25
Test Case 38: Application Primary and Secondary Switch over by Network card unplug.....	25
Test Case 39: AMS Application DC to DR Switch over	26
Test Case 40: Testing of Alarms in AMS	26
Test Case 41: Negative Scenarios – Alarm Simulation	27
Test Case 42: Scheduling of Reports in AMS	27
Test Case 43: PM Files Generation from AMS.....	28
Test Case 44: Interoperability with Third Party ONTs	28
Test Case 45: ONT WAN Configuration through AMS.....	29
Test Case 46: 72 hours Stability of Application	29
Test Case 47: Max Peak Capacity of Application	30
Test Case 48: Full Load Testing of AMS	30
Test Case 49: AMS-OEM product documentation	31
Test Case 50: All credential of the product to be handed over	31
Test Case 51: Solution Document	32
Test Case 52: AMS APIs Execution	32
3 Document Acceptance	34



1 Introduction

This user acceptance test plan provides tests to be performed on the Nokia AMS (Access Management System) domain controller cum AMS/NMS platform to evaluate the management, control and planning functionalities being offered for T-Fiber Network


SITE Name & Address	TNOC-DC
IP Address	172.28.39.11, 172.28.39.12, 172.28.39.13, 172.28.39.14
AMS Host Name	tfdcnokems1, tfdcnokems2, tfdcnokems3, tfdcnokems4
AMS Host ID	1cac0b07, 1cac0c07, 1cac0d07, 1cac0e07
OS Release	Red Hat Enterprise Linux Server release 7.7

SITE Name & Address	DR
IP Address	172.28.7.134, 172.28.7.135, 172.28.7.136, 172.28.7.137
AMS Host Name	tfdrnokems1, tfdrnokems2, tfdrnokems3, tfdrnokems4
AMS Host ID	1cac8607, 1cac8707, 1cac8807, 1cac8907
OS Release	Red Hat Enterprise Linux Server release 7.7




2 Test Cases

Test Setup:

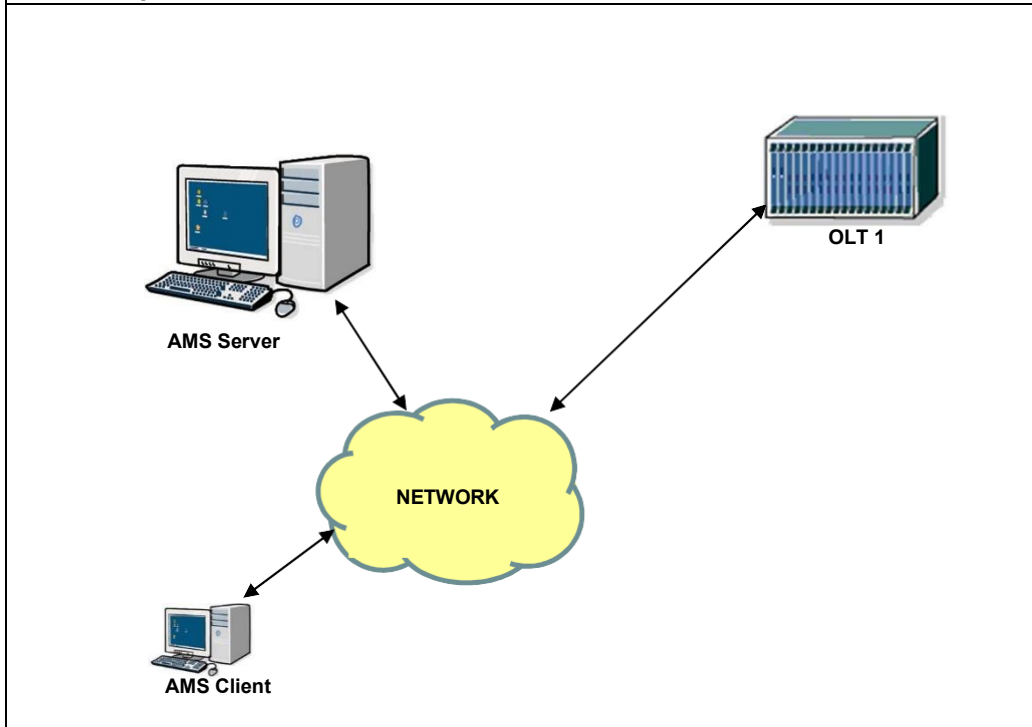

IPs used at Server side.

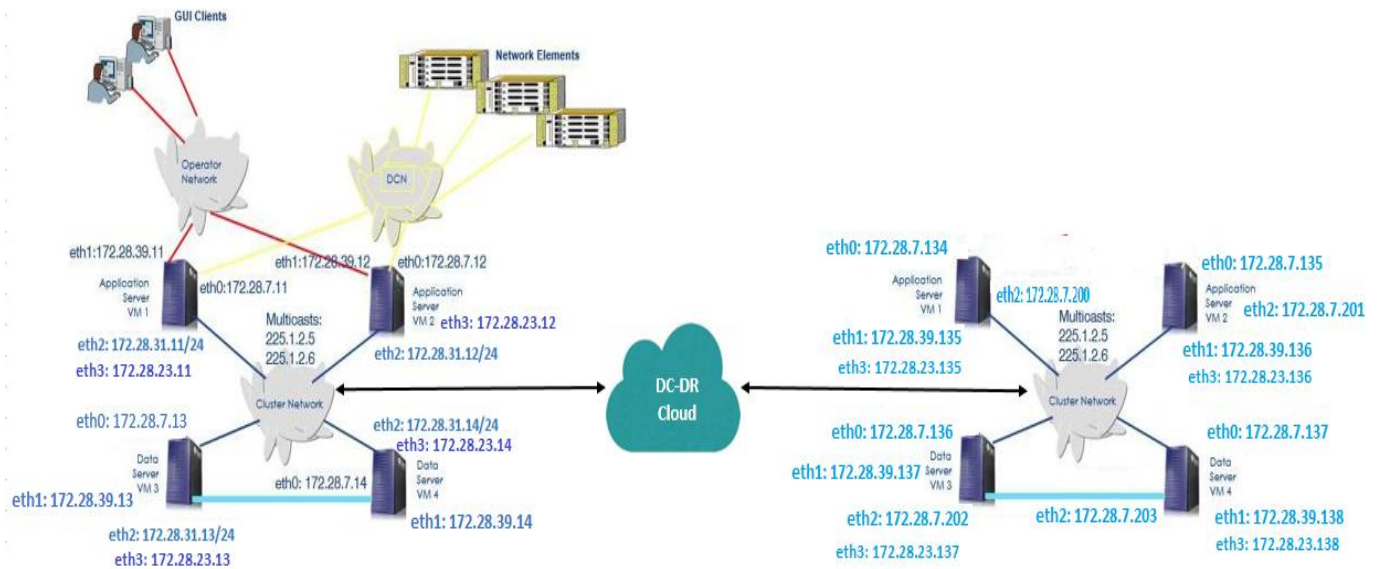



Test Case 1: Validation of IP address for AMS application primary, secondary and DR

Description:	Validation of IP address for AMS application primary, secondary and DR servers
Procedure:	Login to the servers, run the command 'ifconfig' and verify the IP details assigned to VM
Expected Result:	To view assigned IP details in VM
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 2: AMS Server Storage Sizing and Utilisation

Description:	AMS server storage sizing and utilisation
Procedure:	Login to the servers, run the command 'df -kh' and verify the storage details assigned to VM and consumed
Expected Result:	To view assigned and consumed storage details of the servers
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 3: Verify Application Version details

Description:	To verify the Application version details
Procedure:	Login to AMS Click on Help and click on About 5520 AMS
Expected Result:	AMS Application Version details to be displayed
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 4: AMS application License Verification

Description:	AMS application licenses verification
Procedure:	Go to Administrative Tree > License Management
Expected Result:	Should view AMS License
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 5: OLT Addition in AMS

Description:	Addition of OLT in AMS
Procedure:	Login to AMS <u>NE Creation</u> Goto Network Perspective> Right click on group network>create NE>Select the product & release>Input necessary details of node>Click finish <u>NE Supervision</u> Right Click NE>Supervision>Start.
Expected Result:	OLT should be added in AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 6: OLT Deletion in AMS

Description:	Deletion of ONT in AMS
Procedure:	<u>NE Supervision</u> Right Click NE>Supervision>Stop <u>NE Deletion</u> Goto Network Perspective> Click on group network>create NE>Right Click on OLT and Delete
Expected Result:	OLT should be deleted from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 7: ONT Addition

Description:	Addition of ONT in a OLT from AMS
Procedure:	<u>ONT Adding</u> Click NE>Rack1>Subrack1>Slot LT>Pon Port>Right click on ONT (provisioned)>create ONT>enter the necessary Details>Click on Finish
Expected Result:	ONT should be added in OLT
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 8: ONT Deletion

Description:	Deletion of ONT in a OLT from AMS
Procedure:	<u>ONT Deleting</u> Click NE>Rack1>Subrack1>Slot LT>Pon Port>ONT (provisioned)>Right Click on ONT>Delete
Expected Result:	ONT should be deleted in OLT
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 9: OLT Location Name Modification in AMS

Description:	Addition of OLT in AMS
Procedure:	Login to AMS <u>NE Addition</u> Go to OLT > in objects modify the alias name
Expected Result:	OLT location name to be modified
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 10: Node Reachability Test

Description:	Testing of OLT reachability in AMS
Procedure:	1. Make down the OLT by powering off or disconnecting OLT uplink fiber 2. OLT status has to change to Unreachable in AMS(will take 5-6 mins for status change) 3. Make OLT up 4. OLT status has to change to Reachable in AMS(will take 4-5 mins for status change)
Expected Result:	OLT status should change as per the OLT reachability to AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 11: ONT Status Test in AMS (Dying Gasp Alarm)

Description:	Testing of ONT status in AMS
Procedure:	1. Make down the ONT by powering off 2. ONT operational status changes to Down in AMS 3. Dying Gasp alarm will generate on respective ONT 4. Make ONT up 5. ONT operational status changes to Up in AMS
Expected Result:	ONT status should change as per the ONT reachability
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 12: ONT Serial Number Modification from AMS

Description:	Modifying the ONT serial number from AMS
Procedure:	1. Login to AMS 2. Click NE>Rack1>Subrack1>Slot LT>Pon Port>ONT (provisioned)>Select the ONT 3. Make ONT Administrative Stae to Locked 4. Modify the Serial Number of the ONT 5. Make ONT Administrative Stae to Unlocked
Expected Result:	ONT serial number should be modified from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 13: Service Configuration from AMS With Vlan Translation in Bridge Mode

Description:	Service Configuration from AMS for GI-BB/Rythuvédika with VLAN Translation
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 14: Service Configuration from AMS Without Vlan Translation in Bridge Mode

Description:	Service Configuration from AMS for T-DIA/L2VPN/L3VPN without VLAN Translation
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 15: Service Configuration from AMS with Vlan Translation for Route Mode

Description:	Service Configuration from AMS for GI-BB/Rythuvédika service
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 16: Service Configuration from AMS Without Vlan Translation for Route Mode

Description:	Service Configuration from AMS for T-DIA/L2VPN/L3VPN service
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 17: Service Configuration from AMS in Bridge Mode Tagged

Description:	Service Configuration from AMS for GI-BB/T-DIA/L2VPN/L3VPN without VLAN Translation
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 18: Service Configuration from AMS for Q&Q services

Description:	Service Configuration from AMS for Household service
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on VEIP Port > Create > UNI > Finish Under VEIP Port > expand Upstream Queues > map bandwidth profile > Apply Under VEIP Port > expand Downstream Queues > map bandwidth profile > Apply Under VEIP Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 19: Configuration from AMS for IPv6 Service

Description:	Service Configuration from AMS for IPV6 Service
Procedure:	Log in to AMS > Go to respective OLT Pon Port > ONT (Provisioned) > ONT Card > Right Click on Ethernet Port > Create > UNI > Finish Under Ethernet Port > expand Upstream Queues > map bandwidth profile > Apply Under Ethernet Port > expand Downstream Queues > map bandwidth profile > Apply Under Ethernet Port > Right click on UNI > Vlan Association > select Vlan Forwarding Mode > enter vlan and L2 Forwarder vlan details > Finish
Expected Result:	Service should be configured in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 20: Service Deletion from AMS

Description:	Deletion of a Service from AMS
Procedure:	Log in to AMS > Go to respective OLT Pon Port > Expand on ONT > ONT Card > Delete UNI
Expected Result:	Service should be deleted in OLT from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 21: Service Upgradation/Degradation

Description:	Upgrade/Degrade the bandwidth of the service which already configured
Procedure:	Log in to AMS > Go to respective OLT Pon Port > Right click on ONT > UNI > Change Downstream Profiles
Expected Result:	Service has to upgrade/downgrade as per configuration
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 22: User Management with L1, L2, L3 Privileges

Description:	Testing of User Management with L1,L2 and L3 privileges
Procedure:	Create 3 users in Alepo AAA application with L1, L2 and L3 privileges respectively
Expected Result:	User able to login to AMS and should have only assigned privilege in Alepo AAA application
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 23: AMS Password Policies

Description:	Passowrd Policies in AMS
Procedure:	Go to Administrative Tree > User Management > User Settings
Expected Result:	Should view the Password policies in AMS Note: As AMS integrated with Alepo AAA application, password policy is applied by Alepo
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 24: Alarm synchronisation with OSS

Description:	Alarm synchronisation with OSS
Procedure:	1. Generate a alarm in AMS by making OLT/ONT down 2. Login to OSS and check same alarm will refelct in OSS 3. Clear a alarm in AMS by making OLT/ONT up 4. Check alarm is cleared in OSS
Expected Result:	Alarm generated in AMS should reflect in OSS and alarm cleared in AMS should also clear in OSS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 25: OLT/ONT Inventory synchronisation with OSS

Description:	OLT/ONT inventory synchronisation with OSS
Procedure:	1. Add a OLT/ONT in AMS 2. Login to OSS and check same inventory is reflected in OSS inventory 3. Delete a OLT/ONT in AMS 4. In OSS inventory, check deleted inventory will not reflect in OSS Note: OSS is fetching inventory from AMS periodically
Expected Result:	OLT/ONT added in AMS should reflect in OSS and OLT/ONT deleted in AMS should also be deleted in OSS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 26: AMS functionality with syslog server

Description:	Testing of AMS logs in syslog server
Procedure:	Perform the activities like OLT addition/deletion, ONT addition/deletion from AMS. Log in to syslog server, and navigate to respective AMS path /var/log/Remote-Hosts/tfdcnokems1/ /var/log/Remote-Hosts/tfdcnokems2/
Expected Result:	Logs should be available in syslog server
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 27: AMS functionality with NTP server

Description:	AMS sync with NTP server
Procedure:	Log in to AMS server and check the NTP status by running the below command ntpq -p
Expected Result:	AMS should be in sync with NTP
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 28: OLT/ONT inventory report generation from AMS

Description:	OLT/ONT report generation from AMS
Procedure:	Log in to AMS > Inventory Query > run the required query in the list > download the csv file of the query result
Expected Result:	OLT/ONT report should be generated from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 29: Alarms report generation from AMS

Description:	Alarms report generation from AMS
Procedure:	Log in to AMS > Go to Window > Show View > Alarms > Download CSV
Expected Result:	Alarms report should be generated from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 30: Service inventory report generation from AMS

Description:	Service inventory report generation from AMS
Procedure:	Log in to AMS > Inventory Query > run the required query in the list > download the csv file of the query result
Expected Result:	Service inventory report should be generated from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 31: Bandwidth Profiles report generation from AMS

Description:	Bandwidth profiles mapped to services report generation from AMS
Procedure:	Log in to AMS > Inventory Query > run the required query in the list > download the csv file of the query result
Expected Result:	Bandwidth profiles mapped to services report should be generated from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 32: AMS DB Backup Operation

Description:	To check AMS DB Backup.
Procedure:	Login to server with amssys user and execute <code>ams_backup.sh</code> <code>/amsbackup.tar</code> *path should have user amssys rw privilege.
Expected Result:	Should be able to take AMS DB backup
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 33: AMS DB Backup Restoration

Description:	To restore the AMS with Backup file
Procedure:	1. Login to server with amssys user and execute <code>ams_backup.sh /amsbackup.tar</code> *path should have amssys rw privilege. 2. After DB Backup completed, login to AMS and delete ONT/OLT 3. Restore the AMS with DB backup file 4. After Restoration, earlier deleted ONT/OLT should be present
Expected Result:	Should be able to restore the AMS with DB backup file
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 34: Node Backup Procedure

Description:	OLT Backup from AMS
Procedure:	Goto Network Perspective> Click on group network> Right click on OLT > Backup
Expected Result:	OLT backup should happen from AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 35: ONT Upgrade from AMS

Description:	ONT software upgrade from AMS
Procedure:	Goto Network Perspective> Click on group network> Right click on OLT > Software > ONT > Download to OLT > select version > click finish After finishing download Click on OLT > Pon Port > ONT > Planned Software > Auto Click on OLT > Pon Port > ONT > Downloaded Software > Auto
Expected Result:	ONT should come up with upgraded version
Result:	☐ OK ☐ NOK
Logs/Snaps: (if Any)	

Test Case 36: Application Primary and Secondary Switch over by server shutdown

Description:	When both Primary and Secondary AMS is running fine, switch over from Primary to Secondary by shutting down the server
Procedure:	Login into AMS GUI -> Check the HA configuration ->Check the Status of Server under Administration Tree. Shut down the Master DB VM Login Again to AMS GUI → Check the Status of Server under Administration Tree. Shut down the Master App VM Login Again to AMS GUI → Check the Status of Server under Administration Tree.
Expected Result:	Should be able to login into AMS GUI Should be able to login into AMS GUI without needing to input the IP of another application server and able to perform the operations in AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 37: Application Primary and Secondary Switch over by server reboot

Description:	When both Primary and Secondary AMS is running fine, switch over from Primary to Secondary by rebooting the server
Procedure:	Login into AMS GUI -> Check the HA configuration ->Check the Status of Server under Administration Tree. Reboot the Master DB VM Login Again to AMS GUI → Check the Status of Server under Administration Tree. Reboot the Master App VM Login Again to AMS GUI → Check the Status of Server under Administration Tree.
Expected Result:	Should be able to login into AMS GUI Should be able to login into AMS GUI without needing to input the IP of another application server and able to perform the operations in AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 38: Application Primary and Secondary Switch over by Network card unplug

Description:	When both Primary and Secondary AMS is running fine, switch over from Primary to Secondary by unplugging the Network card
Procedure:	Login into AMS GUI -> Check the HA configuration ->Check the Status of Server under Administration Tree. Unplug the network card from the Master DB VM Login Again to AMS GUI → Check the Status of Server under Administration Tree. Unplug the network card from the Master App VM Login Again to AMS GUI → Check the Status of Server under Administration Tree.
Expected Result:	Should be able to login into AMS GUI. Should be able to login into AMS GUI without needing to input the IP of another application server and able to perform the operations in AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 39: AMS Application DC to DR Switch over

Description:	AMS Application switch over from DC to DR
Procedure:	Login into AMS GUI -> Check the HA configuration ->Check the Status of Server under Administration Tree. Shut down the Secondary DB VM → Check the Status of Server under Administration Tree. Shut down the Secondary App VM → Check the Status of Server under Administration Tree. Shut down the Primary DB VM → Check the Status of Server under Administration Tree. Shut down the Primary App VM → Login to DR server → Stop the services running in DR server → Make DR server as active → Start the services in DR
Expected Result:	Should be able to login into AMS GUI and able to perform the operations in AMS.
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 40: Testing of Alarms in AMS

Description:	Testing of Alarms in AMS
Procedure:	Generate the alarms as mentioned below Remove Fiber from ONT Remove Fiber from the OLT Port Power off and on the OLT Power off and on the ONT
Expected Result:	Alarms should be generated in AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 41: Negative Scenarios – Alarm Simulation

Description:	To show case the negative scenarios
Procedure:	1. Reboot the OLT by powering off – Resource isolation alarm generates in AMS 2. Restore the OLT and veirfy the clearance of alarm along with service restoration 3. Reboot the ONT by powering off – Dying Gasp alarm generates in AMS 4. Restore the ONT and veirfy the clearance of alarm along with service restoration 5. Remove the SFP – alarm generates in AMS 6. Reconnect the SFP and veirfy the clearance of alarm along with service restoration
Expected Result:	Alarms should notify in AMS application
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 42: Scheduling of Reports in AMS

Description:	Reports scheduling in AMS
Procedure:	Go To Scheduler, create a scheduler by selecting report and date,time
Expected Result:	Report should be generated as per scheduled
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 43: PM Files Generation from AMS

Description:	To verify the PM files generation from AMS
Procedure:	Go to respective path in the server where PM files are autosaved Path -> /shared/ams/shared/common/ne/pm/
Expected Result:	PM files should be generated by AMS
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 44: Interoperability with Third Party ONTs

Description:	Addition of third party ONT in a OLT from AMS
Procedure:	ONT Adding Click NE>Rack1>Subrack1>Slot LT>Pon Port>Right click on ONT (provisioned)>create ONT>enter the necessary Details>Click on Finish
Expected Result:	Third party ONT should be added in OLT
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 45: ONT WAN Configuration through AMS

Description:	ONT WAN Configuration from AMS
Procedure:	*This Test Case will be executed with the support of OEM ONT WAN configuration is not supported by AMS/OLT
Expected Result:	
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 46: 72 hours Stability of Application

Description:	Nokia AMS-72 hours stability testing of application
Procedure:	Login to AMS server and run the uptime of the server and capture the result
Expected Result:	Uptime of the AMS server to be captured
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 47: Max Peak Capacity of Application

Description:	To get the max peak capacity of application
Procedure:	OEM provides the max peak capacity of application either through documents or mail communication
Expected Result:	Max peak capacity of application
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 48: Full Load Testing of AMS

Description:	To test the full load of application
Procedure:	OEM provides the confirmation on full load testing of AMS application either through documents or mail communication
Expected Result:	Full Load Testing of AMS application confirmation from OEM
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 49: AMS-OEM product documentation

Description:	Nokia AMS product documentation
Procedure:	To share the Nokia AMS product documentation to T-Fiber team
Expected Result:	Nokia AMS product document to be shared
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 50: All credential of the product to be handed over

Description:	To handover All credential of the AMS to T-Fiber team
Procedure:	To handover All credential of the AMS to T-Fiber team
Expected Result:	To handover All credential of the AMS to T-Fiber team
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	



Test Case 51: Solution Document

Description:	To share the Solution Document
Procedure:	To share the solution document
Expected Result:	To share the solution document
Result:	☐ OK ☐ Not OK
Logs/Snaps: (if Any)	

Test Case 52: AMS APIs Execution

Description:	Execution of AMS application APIs		
Procedure:	Execute the AMS application APIs which are used for NBI integration Below APIs required prerequisite configuration like bandwidth profiles, vlan in OLT to execute.		
Expected Result:	API should execute without any error		
Result:	☐ OK ☐ Not OK		
List of APIs			
Sl. No	API	API is common for	Result
1	API to Add ONT in AMS	All services	☐ OK ☐ Not OK
2	API to Create Service with UNI – VT Route	GI-BB, Rythuvedika	☐ OK ☐ Not OK
3	API to Delete Complete Service	All services	☐ OK ☐ Not OK
4	API to Create Service with UNI – VT Bridge	GI-BB, Rythuvedika	☐ OK ☐ Not OK
5	APT to Create Service with UNI – VT Bridge Tag	GI-BB	☐ OK ☐ Not OK
6	API to Create Service without VT – Bridge Untag	T-DIA, L2VPN & L3VPN	☐ OK ☐ Not OK
7	API to Create Service without VT – Route	T-DIA, L2VPN & L3VPN	☐ OK ☐ Not OK
8	API to Create Service without VT - Bridge Tag	T-DIA, L2VPN & L3VPN	☐ OK ☐ Not OK
9	API to Create Q&Q Service – Route	Household Services	☐ OK ☐ Not OK
10	API to Create Q&Q Service – Bridge Tag	Household Services	☐ OK ☐ Not OK
11	API to Create Q&Q Service – Bridge UnTag	Household Services	☐ OK ☐ Not OK



Logs/Snaps: (if Any)



3 Document Acceptance

Organization	MSI Representative	TPA Representative	T-Fiber Representative
Signature			
Name			
Designation			
E-mail ID			
Phone Number			
Date			
